

ORDERING INFORMATION

MODEL : 47LM

PLEASE FILL IN THIS SECTION



Model
Company
Name
P/O No.

FACTORY USE ONLY



Job No.	Approved by (Sales office)
Ser No.	Issued by (Sales office)
Sales	Approved by (Factory)
	Set by (Factory)
Ser No.	

Specify the items you want to change. Default setting will be used if not specified.


DEFAULT shows values in case of nothing specified.

■ SCALING SETTING


ITEM	AVAILABLE RANGE		SET VALUE	DEFAULT VALUE	Factory Internal check	
Scaling Setting Mode → Display Scaling Value A → Display Scaling Value B	Specify the value within the range.	A*	Display Scaling Value A (-9999 – 9999)		-10.00	<input type="checkbox"/> Checked
		B*	Display Scaling Value B (-9999 – 9999)		10.00	

* About scaling point 'A' and 'B.'
 Note: Input scaling is set with 'Teach Calibration.'

- Normal Scaling
 The display value increases when the input signal increases.

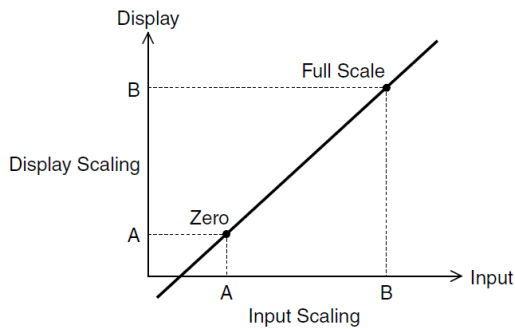

- Inverted Scaling
 The display value decreases when the input signal increases.

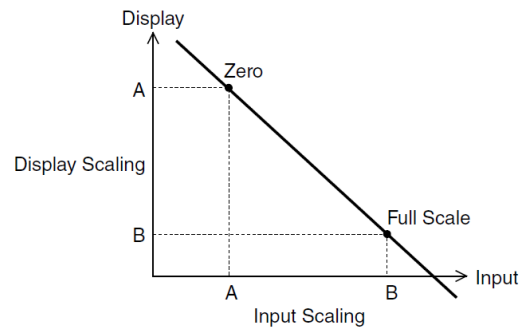

Set the decimal point according to the necessary accuracy.

■ ALARM SETTING

ITEM	AVAILABLE RANGE		SET VALUE	DEFAULT VALUE	Factory Internal check
Alarm Setting Mode → LL Setpoint (only for 4-point alarm output)	-9999 – 9999 (Decimal point is disregarded.) '----' for None Alarm	Specify the value within the range.		-8.00	<input type="checkbox"/> Checked
Alarm Setting Mode → L Setpoint	-9999 – 9999 (Decimal point is disregarded.) '----' for None Alarm	Specify the value within the range.		-4.00	
Alarm Setting Mode → H Setpoint	-9999 – 9999 (Decimal point is disregarded.) '----' for None Alarm	Specify the value within the range.		4.00	
Alarm Setting Mode → HH Setpoint (only for 4-point alarm output)	-9999 – 9999 (Decimal point is disregarded.) '----' for None Alarm	Specify the value within the range.		8.00	

Note: When scaling setting is specified and alarm setting is not specified, L and LL are set to display scaling value A, H and HH are set to display scaling valued B.

■ ENGINEERING UNIT STICKER LABEL

ITEM	AVAILABLE RANGE		SET VALUE	DEFAULT VALUE	Factory Internal check
Engineering unit	DC, AC, mV, V, kV, μA, mA, A, kA, mW, W, kW, var, kvar, Mvar, VA, Hz, Ω, kΩ, MΩ, cm, mm, m, m/sec, mm/min, cm/min, m/min, m/h, m/s ² , inch, ℓ, ℓ/s, ℓ/min, ℓ/h, m ³ , m ³ /sec, m ³ /min, m ³ /h, Nm ³ /h, N-m, N/m ² , g, kg, kg/h, N, kN, Pa, kPa, MPa, t, t/h, °C, °F, %RH, J, kJ, MJ, rpm, sec, min, min ⁻¹ , pH, %, ppm	Select one if necessary.		none	<input type="checkbox"/> Checked

*Location of the sticker label

